



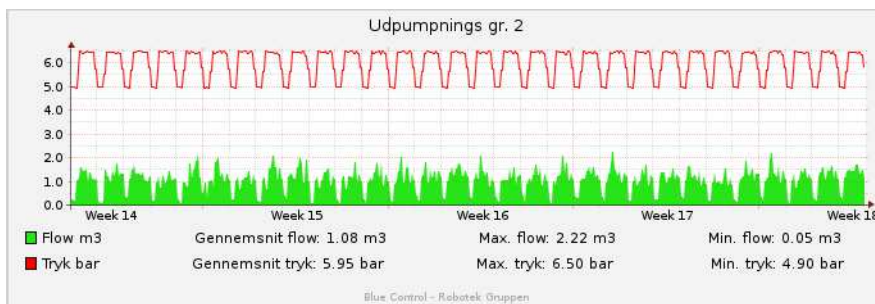

Føllenslev Vandværk

Månedssrapport 04-2014

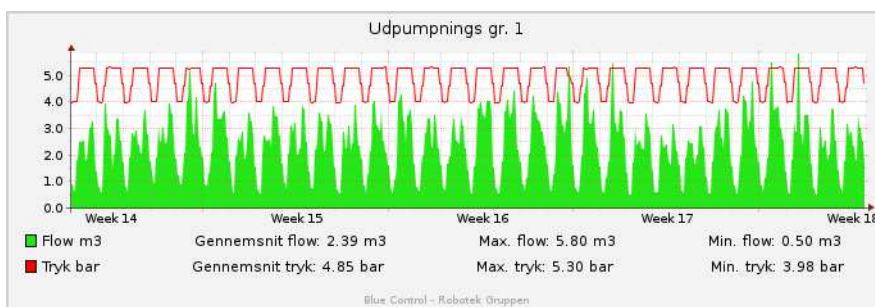

Mængder

Udpumpet vandmængde:	Total: 2525 m ³	Måler 1: 1739 m ³	Måler 2: 786 m ³
Indvundet vandmængde:	Total: 2518 m ³	Måler 3: 2518 m ³	

Forbrug

Elforbrug:	Total: 1986 kWh		
	Total: 0.79 kWh/m ³	Udpumpet:	0.53 kWh/m ³

Flow

Flow måler 1:

Min. Flow:	0.00 m ³ /h	Tidspunkt: 01-04-14 00:29:47
Max. Flow:	14.75 m ³ /h	Tidspunkt: 19-04-14 19:14:46

Flow måler 2:

Min. Flow:	0.00 m ³ /h	Tidspunkt: 01-04-14 00:00:00
Max. Flow:	5.99 m ³ /h	Tidspunkt: 13-04-14 00:07:52

Niveauer i boreriger:

Boring 1 niveau:	Højest: -5.00 m	Lavest: -13.02 m	Sænkning: 8.02 m
Boring 2 niveau:	Højest: -3.36 m	Lavest: -6.78 m	Sænkning: 3.42 m
Boring 3 niveau:	Højest: -3.21 m	Lavest: -6.08 m	Sænkning: 2.87 m

Filter:

Filter 1:	Antal skyl:	8
Filter 2:	Antal skyl:	4

Drifttimer:

	Periode:	Total:
Boring 1:	39 Timer	901 Timer
Boring 2:	146 Timer	1874 Timer
Boring 3:	105 Timer	1613 Timer
Pumpe 1:	420 Timer	6727 Timer
Pumpe 2:	416 Timer	6982 Timer
Pumpe 3:	424 Timer	6641 Timer
Pumpe 4:	423 Timer	6522 Timer
