



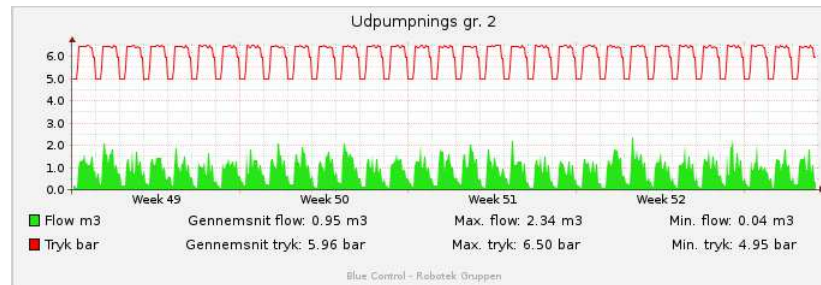

Føllenslev Vandværk

Månedsrapport 12-2013

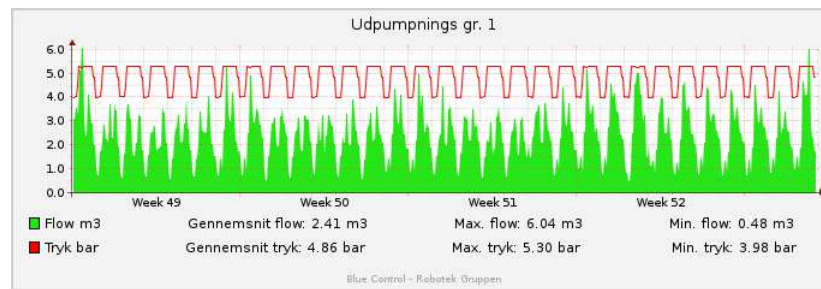

Mængder

Udpumpet vandmængde:	Total: 2470 m ³	Måler 1: 1769 m ³	Måler 2: 701 m ³
Indvundet vandmængde:	Total: 2444 m ³	Måler 3: 2444 m ³	

Forbrug

Elforbrug:	Total: 1938 kWh		
	Total: 0.78 kWh/m ³	Udpumpet:	0.54 kWh/m ³

Flow

Flow måler 1:

Min. Flow:	0.00 m ³ /h	Tidspunkt: 01-12-13 11:49:02
Max. Flow:	11.69 m ³ /h	Tidspunkt: 02-12-13 13:12:15

Flow måler 2:

Min. Flow:	0.00 m ³ /h	Tidspunkt: 01-12-13 00:00:21
Max. Flow:	5.94 m ³ /h	Tidspunkt: 25-12-13 08:54:53

Niveauer i boreriger:

Boring 1 niveau:	Højest: -5.24 m	Lavest: -13.40 m	Sænkning: 8.16 m
Boring 2 niveau:	Højest: -3.73 m	Lavest: -7.25 m	Sænkning: 3.52 m
Boring 3 niveau:	Højest: -3.43 m	Lavest: -6.66 m	Sænkning: 3.23 m

Filter:

Filter 1:	Antal skyl:	8
Filter 2:	Antal skyl:	4

Drifttimer:

	Periode:	Total:
Boring 1:	33 Timer	716 Timer
Boring 2:	142 Timer	1338 Timer
Boring 3:	117 Timer	1173 Timer
Pumpe 1:	406 Timer	5114 Timer
Pumpe 2:	434 Timer	5298 Timer
Pumpe 3:	419 Timer	4953 Timer
Pumpe 4:	420 Timer	4854 Timer
