



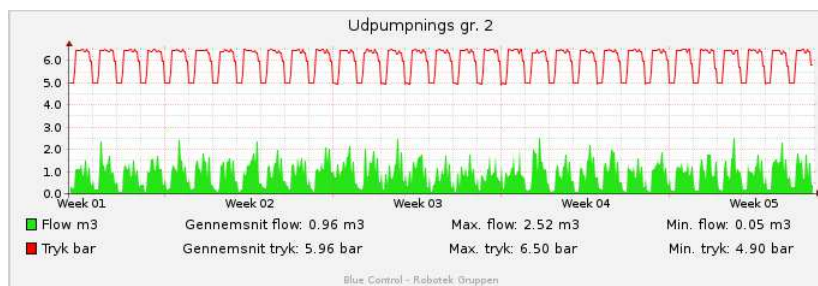

Føllenslev Vandværk

Månedsrapport 01-2014

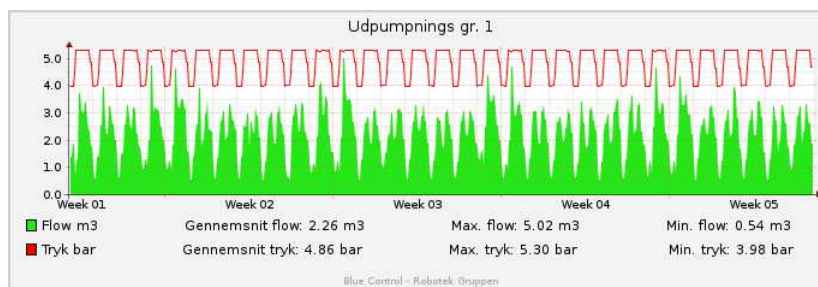

Mængder

Udpumpet vandmængde:	Total: 2466 m ³	Måler 1: 1731 m ³	Måler 2: 735 m ³
Indvundet vandmængde:	Total: 2442 m ³	Måler 3: 2442 m ³	

Forbrug

Elforbrug:	Total: 1970 kWh		
	Total: 0.80 kWh/m ³	Udpumpet:	0.55 kWh/m ³

Flow

Flow måler 1:

Min. Flow:	0.00 m ³ /h	Tidspunkt: 01-01-14 00:02:18
Max. Flow:	11.85 m ³ /h	Tidspunkt: 04-01-14 09:26:24

Flow måler 2:

Min. Flow:	0.00 m ³ /h	Tidspunkt: 01-01-14 00:00:09
Max. Flow:	6.09 m ³ /h	Tidspunkt: 09-01-14 15:57:15

Niveauer i boringer:

Boring 1 niveau:	Højest: -5.00 m	Lavest: -13.12 m	Sænkning: 8.12 m
Boring 2 niveau:	Højest: -3.48 m	Lavest: -6.93 m	Sænkning: 3.45 m
Boring 3 niveau:	Højest: -3.29 m	Lavest: -6.30 m	Sænkning: 3.01 m

Filter:

Filter 1:	Antal skyl: 7
Filter 2:	Antal skyl: 3

Drifttimer:

	Periode:	Total:
Boring 1:	44 Timer	760 Timer
Boring 2:	134 Timer	1471 Timer
Boring 3:	112 Timer	1280 Timer
Pumpe 1:	418 Timer	5529 Timer
Pumpe 2:	431 Timer	5717 Timer
Pumpe 3:	443 Timer	5395 Timer
Pumpe 4:	428 Timer	5270 Timer
